
ST-VDC-01 | Session 08 - Device / Junction-Box Layout

Snowdon Towers independent educational electrical VDC capstone | FINAL QA EVIDENCE RECORD | 2026-10-02


Status	COMPLETE - QA PASSED
Scoped quantity	8 total: six receptacles (R1-R6) + two 120 V junction boxes (J1-J2)
Working view	L1 Electrical Overhead
Model	ST-VDC-01_Electrical_Isaak_v001.rvt - saved at Session 8 closeout
Next session	S09 - electrical relationships, schedule, warnings review, Gate 1

Evidence A - overhead junction boxes

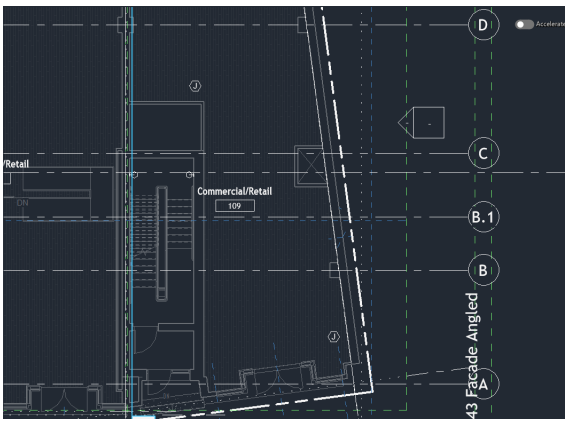

Dedicated Level 1 overhead electrical view showing the two scoped junction-box locations. J1 and J2 are 120 V educational-model distribution points positioned just below the overhead slab.

Evidence B - receptacle scope

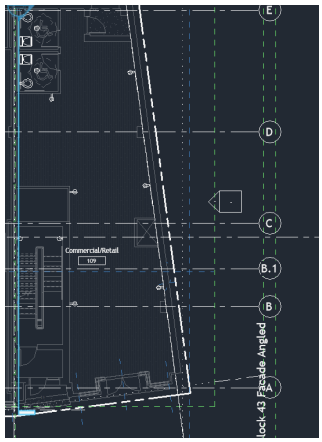

Level 1 plan capture showing all six scoped receptacles: three on the east side and three on the west side. Instances were marked R1-R6 during QA closeout.

Session 8 exit-criteria check

Requirement	Result
8-12 devices/J-boxes in scoped zone	PASS - 8 total
Marks / useful identity parameters	PASS - R1-R6 and J1-J2
Plan evidence of complete scope	PASS - paired overhead and receptacle plan captures
3D / overhead sanity check	PASS - junction-box locations reviewed in 3D and overhead view
Saved working model	PASS - RVT saved at closeout

Limitations: independent educational work using Autodesk sample models; not for construction. Junction-box mounting/support, final circuit relationships, raceway routing, engineering criteria, and code compliance are not claimed by this milestone.
