
Primary conduit layout

Session 10 closeout | Isaak Meakin | October 6, 2026

Initial-route milestone complete. Equipment-room conduit routes and the route from P-208-1 to one Level 1 junction box are documented. Isaak confirmed the working RVT was saved and backed up.

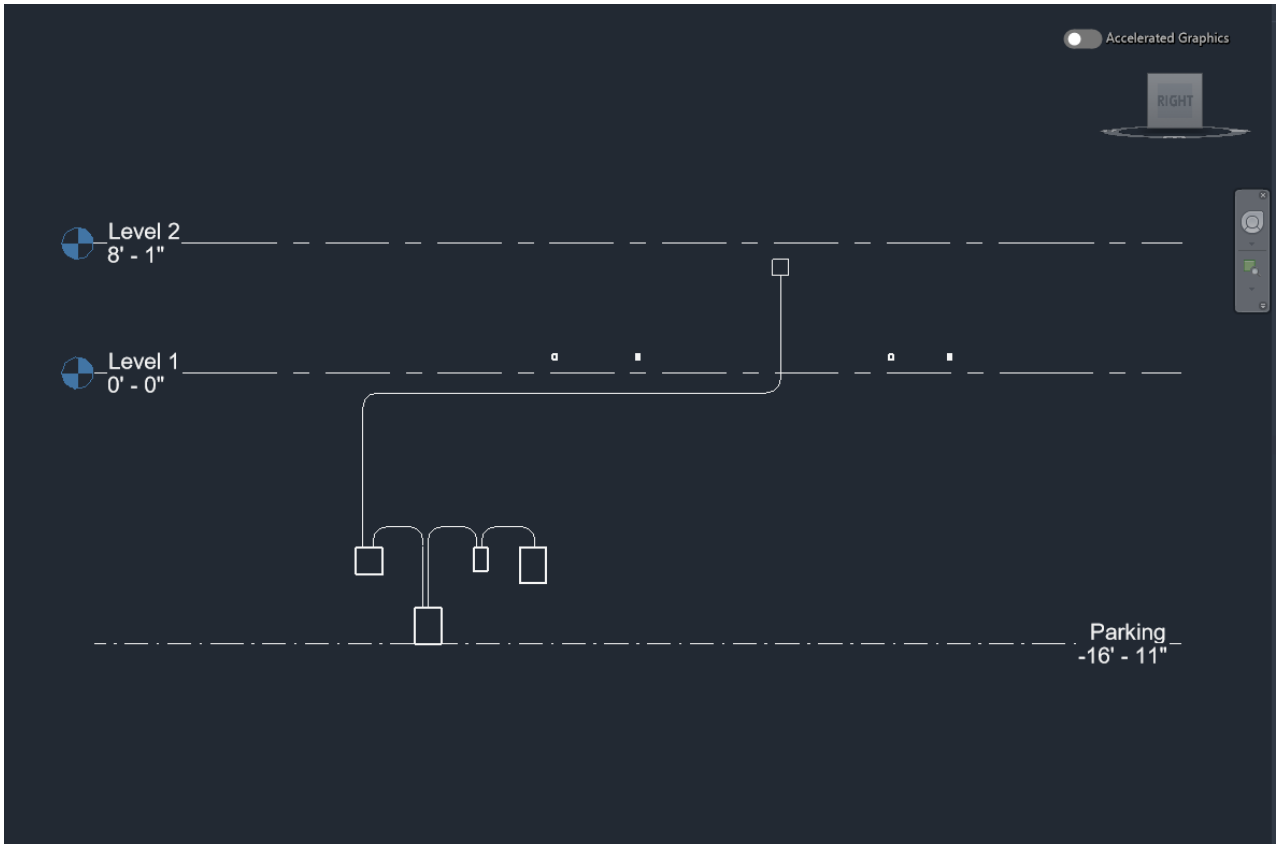

C024 - Right-oriented 3D view. Architectural and HVAC links are hidden to show the electrical scope. This capture shows routing geometry; it does not establish clearance or clash approval.

Sampled segment	Reference level	Centerline / middle elevation
Equipment-room horizontal	Parking	7'-4"
Main horizontal distribution	Parking	15'-8 21/256"
Junction-box vertical	Level 1	Upper 6'-1"; lower -0'-0 81/256"


Conduit: all three sampled segments show 2 in trade diameter, Electrical Metallic Tubing (EMT), Conduit without Fittings. Elevations are offsets from each segment's stated reference level.

Properties sources: C021 image(20261007-001259).png; C022 image(20261007-001344).png; C023 image(20261007-001450).png.

Primary conduit layout

Warnings, scope decisions and next action

Two stored warnings - accepted unused ports. Review Warnings identifies connectors #2 and #3 on the same Conduit Junction Box - Tee - Aluminum: Standard instance, element ID 963291.

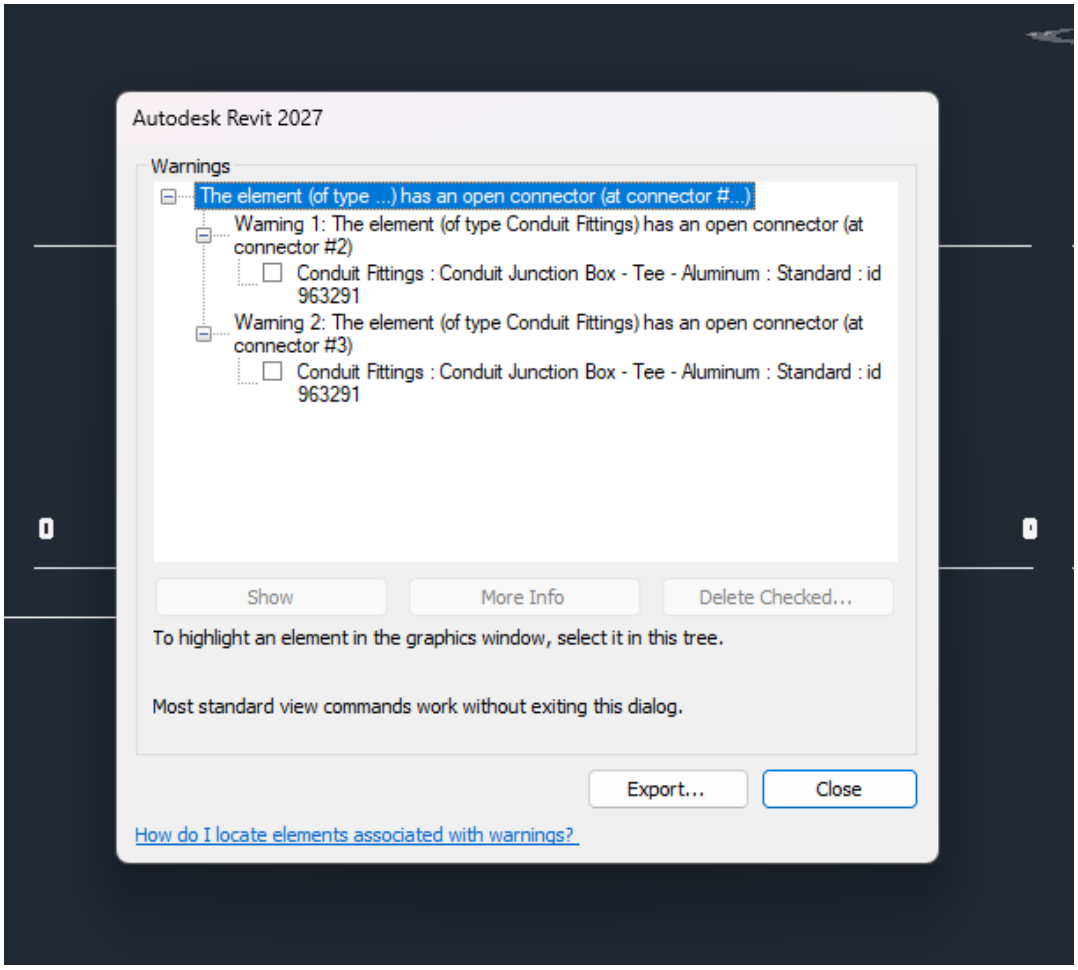

C026 - Stored warning list. The Family Editor capture C025 shows three conduit connectors. One port is used; the other two are unused in the current scope. No other warning categories appear in the supplied list.

Scope revision. Current device scope is six receptacles and one junction box. The earlier S08/S09 two-box records remain historical. Update the device register during S14 QA to match the revised count. Receptacle branch conduit is omitted from the S10 initial-route milestone.

Routing lesson. Equipment spacing and view control affected the first routing attempts. Section views made elevations and alignment easier to inspect. The closeout records actual model properties and identifies unused family ports rather than treating hidden markers as resolved connections.

Next: S11 - overhead conduit rack. Develop a multi-conduit rack with consistent spacing, organized runs and a measurable section for later prefab documentation. Detailed geometry review remains in S12, with phase QA at S14.

Conduit size, bends, supports, conductor fill, protection and working clearances are educational modeling assumptions. This milestone is not engineering or construction approval.
